

Production Engineering Weekly Overview Report

Week 34
16 - 20 February 2026



INDEX

- 1 Departmental Overview (HEAL)
- 2 Nchwaning 3 Performance Overview
- 3 Nchwaning 2 Performance Overview
- 4 Gloria Performance Overview
- 5 BEV Performance Overview
- 6 Utility Performance

DEPARTMENTAL OVERVIEW (HEAL)

↗ Highlights

- ✓ [N2] The average TMM availability improved.
- ✓ [N2] All the emulsion UVs are back to production
- ✓ [N3] Scaler 49 and 51 delivered to site.
- ✓ [GLA] Conveyor Watch submitted the splice condition report and is looking good only small damages need to be fixed
- ✓ [GLA] Scaler audits on brakes after incident in NCHIII – all brakes were operational and good condition

↘ Lowlights

- ⚠ [N2] The UV 137 is switched back to Level 7
- ⚠ [N2] Increased breakdowns on utility LDOs.
- ⚠ [N3] SR0028 brakes failure, found on inspection
- ⚠ [N3] Poor availabilities of DT, FL and HD
- ⚠ [GLA] Shift Foreman stopped the 74N plant due to non compliance
- ⚠ [GLA] DT0106 on breakdown relating to Nerospec


🕒 Emerging Issues

- ⚠ [N2] Electrical reticulation network is getting overloaded
- ⚠ [N3] Spares for S2 and Scalers (engines)
- ⚠ [N3] Roadway conditions
- ⚠ [GLA] UV 0068 Emulsion unit axle to be replace nothing available at the store
- ⚠ [GLA] Commission surface compressor – Challenge 4 inch from the compressor to 2-inch line in the shaft and keep tripping the compressor

🔑 Priorities

- ⚙ [N2] Encourage team effort through VFL and findings.
- ⚙ [N3] Vehicle allocation
- ⚙ [N3] Roadway maintenance strategy
- ⚙ [N3] DT0148 and DT0145 repair (Barlows)
- ⚙ [N3] Appointment of GES and mech foreman
- ⚙ [GLA] 74N tip liners to be repairs
- ⚙ [GLA] CV0053 to do hot splice
- ⚙ [GLA] Remove axle from UV0128 to UV0068

Nchwaning 3 Weekly Availability Trend

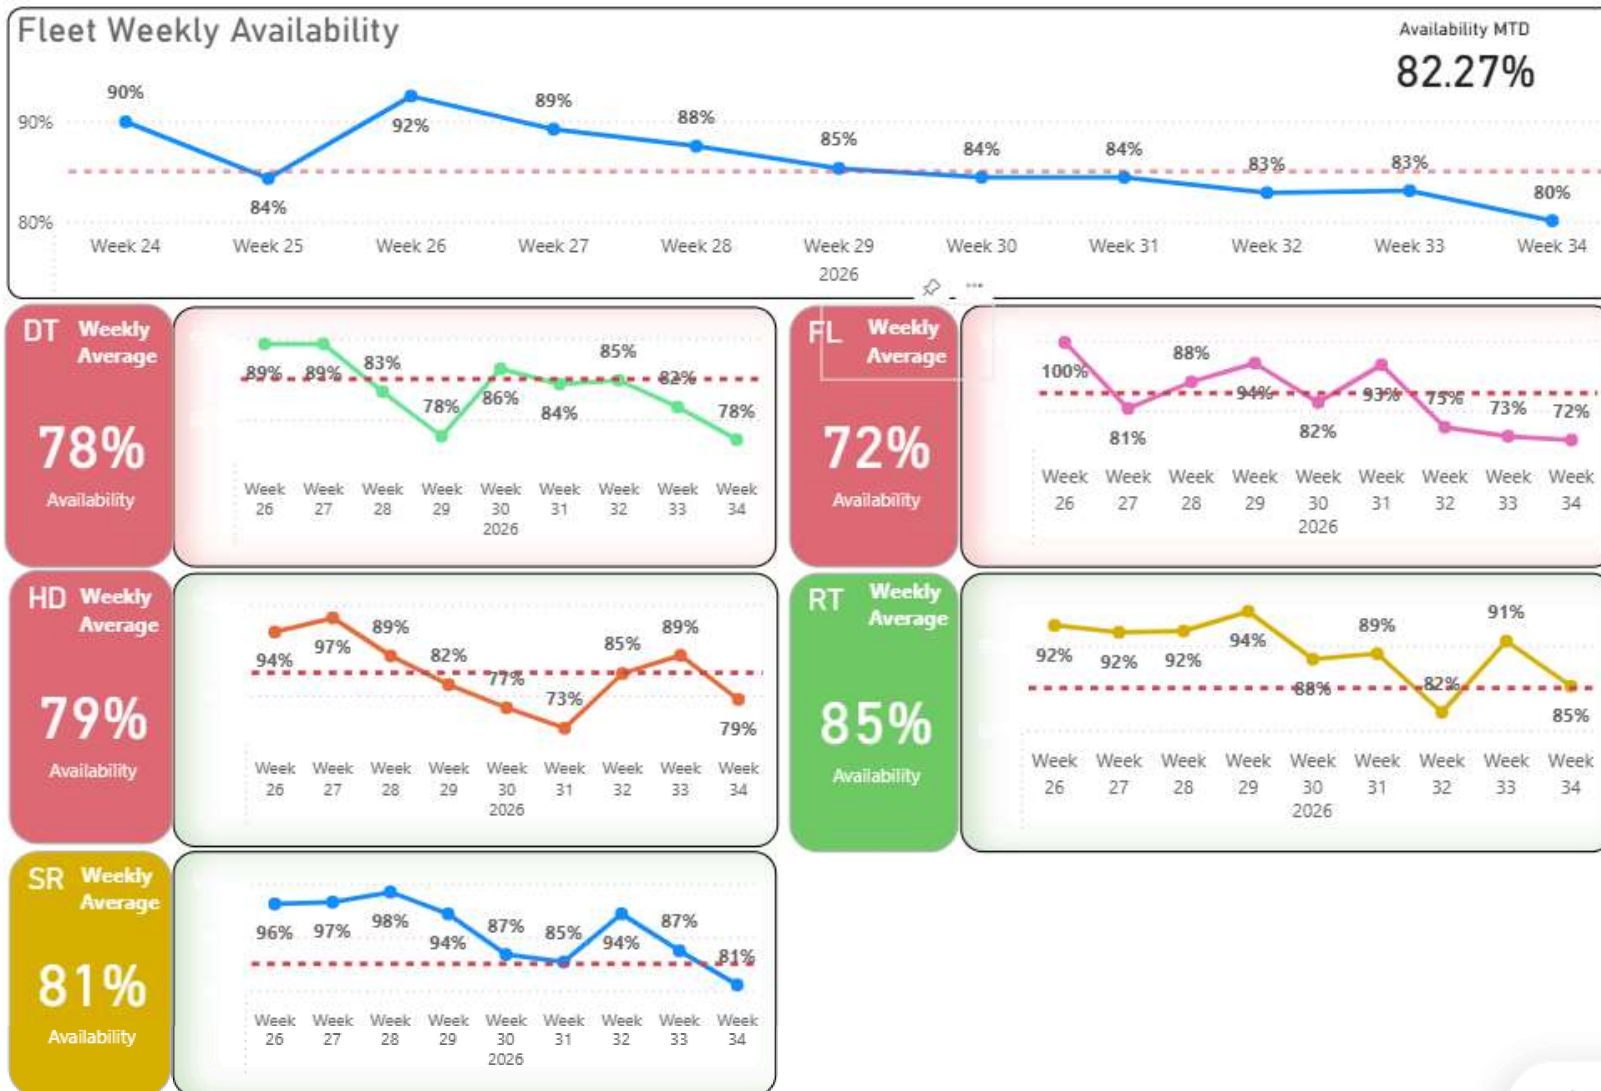

Nchwaning 3 Performance Overview

✓ Safety

Zero incidents this week

Weekly Avg.


79%

(Target: 85%)

⚙ Compliance

SR at 60% (SR0030 Scraped, SR0035 Waiting for engine), Support Equip at 66.7%

Equipment Availability



Key Breakdowns

Dump Trucks (78%): DT148: Aircon/Main switch (spares), DT145: Gears, DT164: Aircon, DT172: HVLI fault

Front Loaders (72%): FL101: Transmission, FL103: Not starting

Hydraulic Drills (79%): HD55: Window damage, HD49: Bosch pump, HD62: Bosch pump, HD61: Cable damage

HD and Scaler availability recovered well over the weekend. 2x New Scalers to be commissioned today. Focus is on getting OEM assistance for FL103, DT145 and DT148 to be resolved this week. FL101 transmission will be completed this week by Mer team.

Nchwaning 2 Weekly Availability Trend



Slicer Date

This Week

Shaft

NCH2

_Prod Day

Yes

Availability

87.65%

Earliest Date Latest Date

2/16/2026 2/20/2026



DT

81.78%

Availability



FL

87.55%


Availability



Load and Haul

85.91%


Availability



HD

88.07%

Availability



Drill and Blast


90.69%

Availability

RT

93.38%

Availability



SR

90.45%

Availability

Nchwaning 2 Performance Overview

✓ Safety

Zero incidents this week

Weekly Avg.

87.65%

(Target: 85%)

🏠 Compliance

DT: 100%, FL: 100%, HD: 75%, RT: 100%, SR: 100%, Support: 100%

Equipment Availability

DT

82%



FL

88%



HD

88%



RT

93%



SR

90%



Key Breakdowns

Dump Trucks (81.78%): DT121: Park Brake (OEM on site)

Gloria Weekly Availability Trend



DT Weekly Average

48%

Availability



FL Weekly Average

88%

Availability



HD Weekly Average

89%

Availability



RT Weekly Average

90%

Availability



SR Weekly Average

87%

Availability



Gloria Performance Overview

✓ Safety

Zero incidents this week

Weekly Avg.

77%

(Target: 85%)

⚙ Compliance

FL: 0% (GD0008 on breakdown), RT: 66.7%,
SR: 50%, Support: 80%

Equipment Availability

DT

48%



FL

88%



HD

89%



RT

90%



SR

87%



Key Breakdowns

DT (48%): DT0174: No revs, DT0173: Transmission timing, DT0106: Nerospec, DT0152: Powerless, DT0153: No acceleration

SR (87%): SR0040: CAS Level 9 installation

BEV Performance Overview (Nchwaning 3)

🔌 BEV Availability (Wk 33)

- DT BEV: 78% (Below Target)
- FL BEV: 90% (Above Target)

⚡ BEV Service Compliance

- DT BEV: 100%
- FL BEV: 100%

BEV Availability by Equipment Type

DT BEV

Target: 85%

78%

FL BEV

Target: 85%

90%

Key BEV & Battery Themes

Performance Summary:

- DT BEV at 78% - below target by 7%. Critical: DT0172 HVIL fault, DT0147 e-stop relays, DT0163 battery connection issues.
- FL BEV at 90% - meets target. Boilermaker work and Strata issues main constraints.

Battery & Charger Status:

- Battery VPY00076 isolation fault affecting FL0099. Isolators between contactors and VCB need replacement.
- All chargers are operational despite Charger 2 Module 2 fault - module bypassed while other modules working.
- B4 Batteries: 9 Working, 1 Breakdown | B5 Batteries: 11 Working, 1 Breakdown, 1 Underground (not commissioned)
- Post 3, 6 and 7 cables replaced. Piet to put in at other chargers.


DT: AVAILABILITY & BREAKDOWNS

⚠ BEV Availability

78%

Goal: 85% (-7.0%)

BEV Availability by Unit

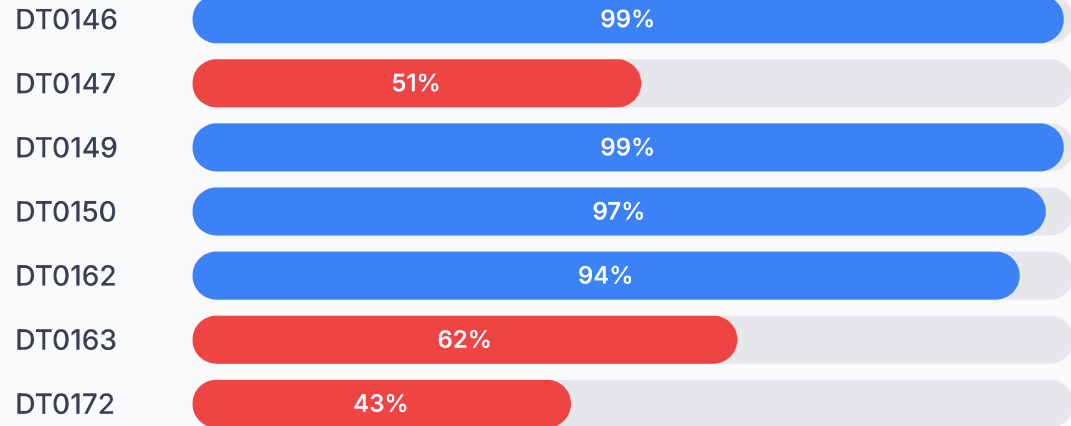

Breakdown Details

Type	Machine_id	Comment	Hours
Electrical	DT0172	HVEL Fault @ Batt Bay	37.17
Electrical	DT0147	Emergency stop @ tramming parking	31.18
Electrical	DT0163	Red Stop Lamb @ Batt Bay	26.38
Mechanical	DT0162	Tyre @ Batt Bay	
Electrical	DT0150	Invertor @ Batt Bay	


FL: AVAILABILITY & BREAKDOWNS

✓ BEV Availability

90%

Goal: 85% (+5.0%)

BEV Availability by Unit

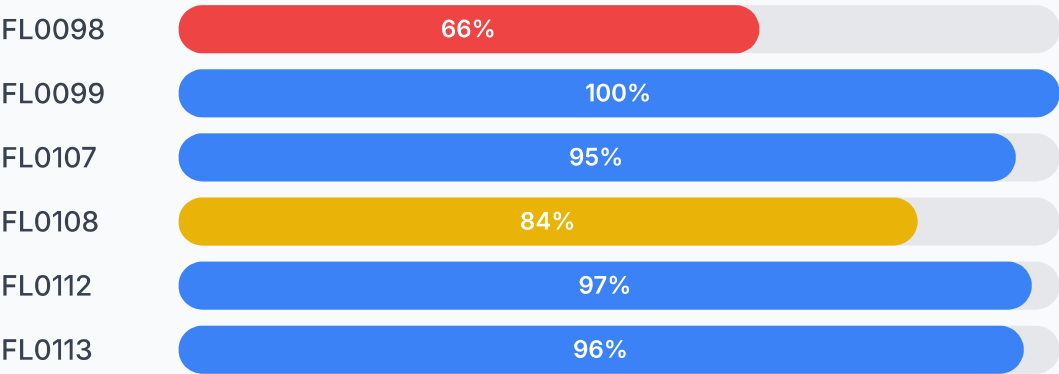

Breakdown Details

Type	Machine_id	Comment	Hours
Mechanical	FL0098	Replace transmission mounting rubbers @ Workshop	47.45
Boilermaker	FL0108	Half Arrows @ boilershop	19.42
Mechanical	FL0107	Tyre @ Batt Bay	7.5
Strata	FL0112	Comms Error @ 49s59w SWD	1.98
Mechanical	FL0113	Oil Leak @ batt bay	

UTILITY SECTION PERFORMANCE OVERVIEW



61

Available

Overall Fleet Availability

94%

61 of 65 units available



4

Unavailable

Area / Owner	Mon	Tue	Wed	Thu	Fri	Weekly Av. Avail.
Main West	1/2	1/2	1/2	1/2	2/2	70.0%
Boilermaker	2/3	2/3	2/3	2/3	2/3	66.7%
BEV	2/2	2/2	1/2	1/2	2/2	80.0%
Security	1/1	1/1	1/1	1/1	1/1	100.0%
Logistics	6/7	6/7	6/7	6/7	6/7	85.7%
Hyd Fitter	6/6	6/6	6/6	6/6	6/6	100.0%
Electricians	3/4	4/4	4/4	4/4	4/4	95.0%
Mechanics	3/3	3/3	3/3	3/3	3/3	100.0%
Sampling	2/2	2/2	2/2	2/2	2/2	100.0%
Construction	3/3	3/3	3/3	3/3	3/3	100.0%
Plant Fitter	6/7	6/7	6/7	6/7	6/7	85.7%
Central	1/2	1/2	1/2	1/2	2/2	70.0%
Explosive	1/1	1/1	1/1	1/1	1/1	100.0%
X Cut	1/1	1/1	1/1	1/1	1/1	100.0%
Utility TMM	2/2	2/2	2/2	2/2	2/2	100.0%
Other	18/18	18/18	18/18	18/18	18/18	100.0%
TOTAL	59/66	61/66	60/66	60/66	62/66	91.5%

UTILITY SECTION: UNAVAILABILITY DETAILS

Week 34 - All Unavailable Units

⚠ Weekly Breakdown Summary

Area/Owner	TMM No.	Model	Description - EOS / Breakdown	Remarks / Comment
Boilermaker	LD0405	Maverick	Not Available	Engine commission (No communication between engine and machine)
Plant Fitter	LD0620	Maverick	Not Available	Strata (Surface decline & No access to gate, locked)
Logistics	UV0078	RORO	Not Available	Rear axle

Note: 1 unit(s) require OEM assistance

UTILITY SECTION CURRENT STATUS

Friday, 07 February 2026

⚠️ Unavailable Units by Area/Owner

Area/Owner	Unavailable	Details (Unit - Reason/Comment)
BEV	1	LD0375 - Clutch / Missing shock (SOS - EOS)
Boilermaker	1	LD0405 - Engine commission (No communication between engine and machine) - No solution from Fermel (Deutz EMR4 upgrade to EMR5)
Main West	1	LD0520 - Front axle (SOS - EOS) - Waiting for parts
Central	1	LD0572 - Not Starting, Emergency brake knob broken off, Ball joint (SOS - EOS) - Waiting for parts

Total Unavailable: 4 units across 4 areas
