

Production Engineering Weekly Overview Report

Week 35
20 - 27 February 2026



INDEX

- 1 Departmental Overview (HEAL)
- 2 Nchwaning 3 Performance Overview
- 3 Nchwaning 2 Performance Overview
- 4 Gloria Performance Overview
- 5 BEV Performance Overview
- 6 Utility Performance

DEPARTMENTAL OVERVIEW (HEAL)

↗ Highlights

- ✓ [N2] DTs are back to full fleet with DT0121 finally fixed
- ✓ [N2] Commissioned a new truck DT0182
- ✓ [N3] Good plant tons over the weekend
- ✓ [GLA] Good improvement in RTs and HDs availability for three weeks
- ✓ [GLA] All CAT trucks are available for production
- ✓ [GLA] MTD production tons above the target by 218 tons

↘ Lowlights

- ⚠ [N2] UV 137 is switched back to Level 7 while the faultfinding
- ⚠ [N3] Poor availabilities on DTs and FLs
- ⚠ [N3 / GLA] PowerBi and Mobiliaris reporting discrepancies
- ⚠ [GLA] Raise compressor failure causing pressure drop resulting SMS not to shotcrete in 9 West section
- ⚠ [GLA] DTs availability was 76%


🕒 Emerging Issues

- ⚠ [N2] 28N electrical trip out are impacting production
- ⚠ [N2] Loading points
- ⚠ [N3] LDV/UV Strata related & allocations
- ⚠ [N3] Brake test winch/ramps
- ⚠ [N3] Scaler brake hub wear
- ⚠ [GLA] UV 0068 Emulsion unit axle to be replace nothing available at the store
- ⚠ [GLA] Commission surface compressor – Challenge compressor trips

🔧 Priorities

- ⚙ [N2] Enforce compliance through action plans
- ⚙ [N2] Discussed report escalation on breakdowns affecting production with the team
- ⚙ [N3] Implement brake test ramps for Scalers
- ⚙ [N3] Roadway meeting
- ⚙ [GLA] 74N tip CAP liners to be repaired – two outstanding
- ⚙ [GLA] CV0053 and 51H to be hot spliced
- ⚙ [GLA] Waiting delivery of diverted actuator for HG and LG

Nchwaning 3 Weekly Availability Trend

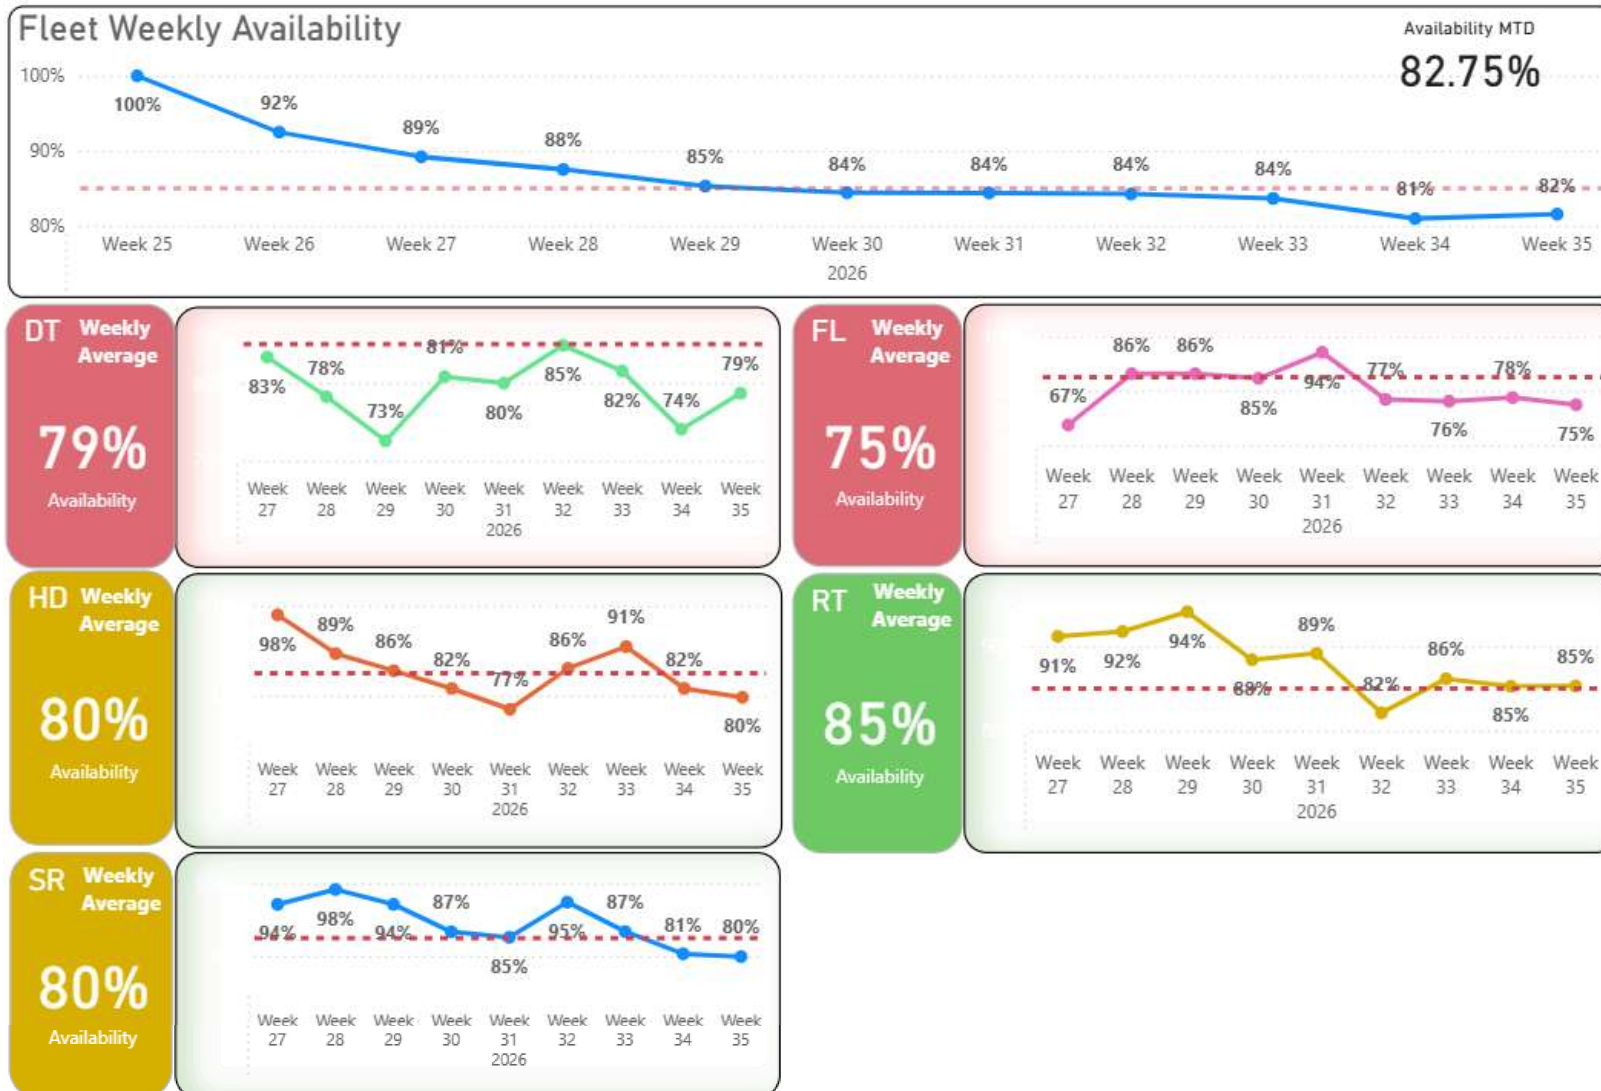

Nchwaning 3 Performance Overview



Safety

Zero incidents this week

Weekly Avg.

82.75%

(Target: 85%)



Compliance

All equipment at 100% compliance

Equipment Availability

DT

79%



FL

75%



HD

80%



RT

85%



SR

80%



Key Breakdowns

Dump Trucks (79%): DT148: Crank seal (Barlows assisting), DT154: Engine not starting, DT145: Wiring(Fixed by Barlows), DT147: Inverter error

Front Loaders (75%): FL101: Steering (Fixed), FL103: Wiring problem (Epiroc assisting)

Hydraulic Drills (80%): HD49: Propshaft, HD61: ECM engine check, HD55: Door & Window damaged

Scalers (80%): SR35: Engine smreplacement (waiting for engine 2 weeks), SR24: Aircon, SR39: Brakes Faulty, SR49 and SR51 commissioned on L7. L9 commissioning to be done nce remainder of Scalers are delivered

Combined DT availability (Diesel + BEV) at 79%. FL at 75%. HD availability at 80%. BEV DT at 81%, BEV FL at 89%. Current outstanding DT = DT0148

Nchwaning 2 Weekly Availability Trend



Slicer Date

Last Week

Shaft

NCH2


_Prod Day

Yes

Availability

90.40%

Earliest Date Latest Date
2/23/2026 2/27/2026

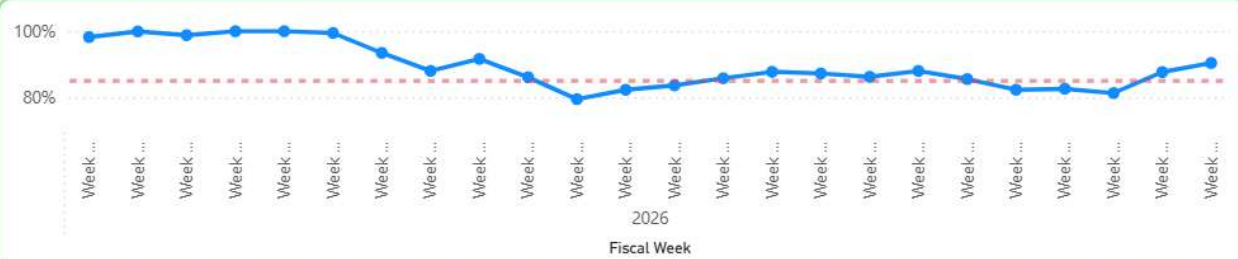

DT

88.08%

Availability



FL

86.29%

Availability



Load and Haul

88.84%

Availability

HD

92.26%

Availability



Drill and Blast

93.02%

Availability

RT

93.79%

Availability



SR

92.36%

Availability



Nchwaning 2 Performance Overview

✓ Safety

Zero incidents this week

Weekly Avg.

90.4%

(Target: 85%)

🔧 Compliance

DT: 100%, FL: 100%, HD: 133%, RT: 100%, SR: 100%, Support: 64%

Equipment Availability

DT

88%



FL

86%



HD

92%



RT

94%



SR

92%




Key Breakdowns

UV0137: Switched back to Level 7 while faultfinding continues

Support Equipment (64%): Support equipment compliance at 64% - Unit 20.19.13

Gloria Weekly Availability Trend

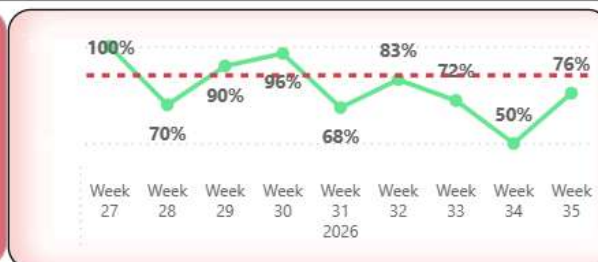

Gloria Performance Overview

✓ Safety

Zero incidents this week

Weekly Avg.

85.28%

(Target: 85%)

🏠 Compliance

DT: 100%, HD: 100%, RT:
100%, UV: 100%, Support:
0%

Equipment Availability

DT

76%



FL

98%



HD

94%



RT

91%



SR

98%



Key Breakdowns

Dump Trucks (76%): DT0105 & DT0106: Nerospec issues, DT0173: Jumping gears

MTD production tons above target by 218 tons. All CAT trucks available for production. Raise compressor failure impacting shotcrete operations in 9 West section.

BEV Performance Overview (Nchwaning 3)

BEV Availability (Wk 33)

- DT BEV: 81% (Below Target)
- FL BEV: 89% (Above Target)

BEV Service Compliance

- DT BEV: 100%
- FL BEV: 100%

BEV Availability by Equipment Type

DT BEV

Target: 85%

81%

FL BEV

Target: 85%

89%

Key BEV & Battery Themes

Performance Summary:

- DT BEV at 81% - below target by 4%. Critical: DT0147 hydraulic oil leak (94hrs) and HV cable fault. DT0163 tyre issues (26hrs).
- FL BEV at 89% - above target by 4%. FL0098 TCU error and mechanical breakdowns (27hrs). FL0108 mechanical breakdown (12hrs). FL0113 Strata and boilermaker work (10hrs).

Battery & Charger Status:

- B4 Batteries: 9 Working, 1 Breakdown (VPY-00076 to be replaced by VPY-00034) | B5 Batteries: 11 Working, 1 Breakdown (VPX-00016 waiting for Scania), 1 on DT-171 (out of production)
- All chargers operational. Charger 2 Module 2 faulty - other modules working. Charger 7 Module 4 switched on.
- TMS hyper care underway. Coolant pump failures - new pumps ordered, arriving 07 March. Changing coolant and hoses on


DT: AVAILABILITY & BREAKDOWNS

⚠ BEV Availability

81%

Goal: 85% (-4.0%)

BEV Availability by Unit

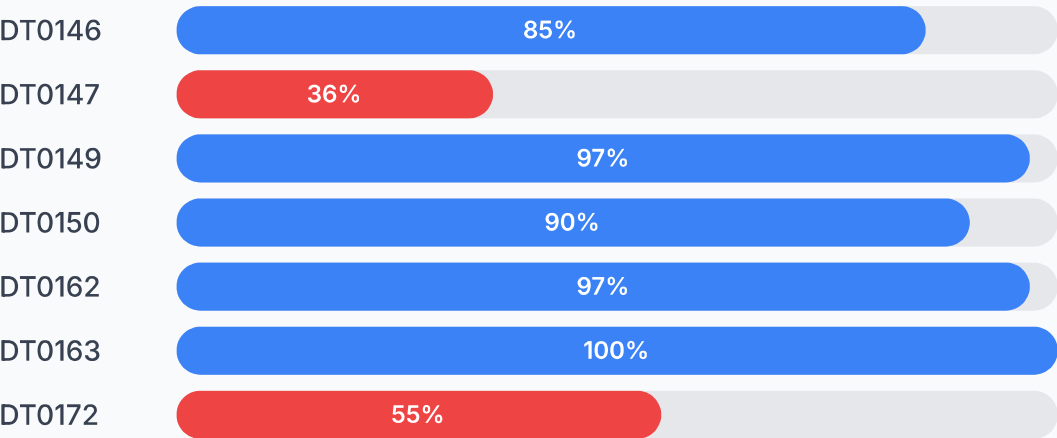

Breakdown Details

Type	Machine_id	Comment	Hours
Mechanical	DT0147	Inverter error and Hydraulic oil leak @ battery bay	96.74
Electrical	DT0172	HVIL fault	72
Strata	DT0146	Collision avoidance warning @ battery bay	24.6
Tyre Bay	DT0163	Tyre bay change rear tyre	14.17
Electrical	DT0150	Battery insulation fault @ 31W/54S R5	11.25


FL: AVAILABILITY & BREAKDOWNS

✓ BEV Availability

89%

Goal: 85% (+4.0%)

BEV Availability by Unit

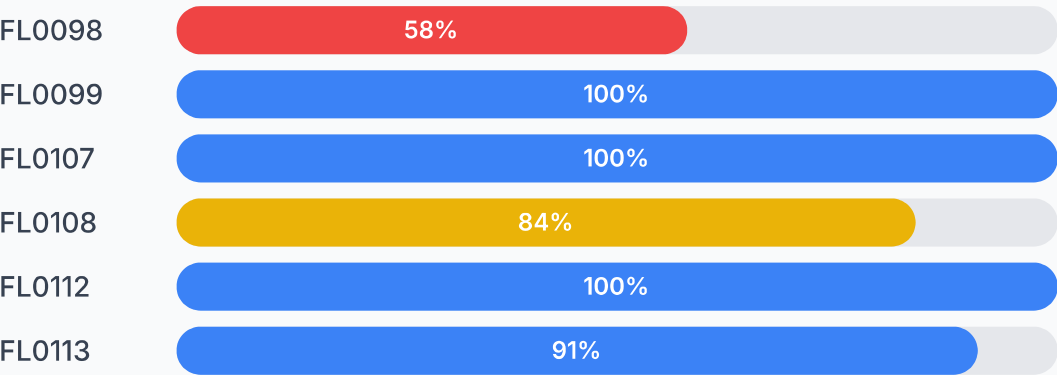

Breakdown Details

Type	Machine_id	Comment	Hours
Electrical	FL0098	Batt not connecting @ S2N Wplace	44.15
Electrical	FL0098	Module error F204 fuse @ S2N	11.5
Mechanical	FL0098	Centre bearing @ battery bay	6.18
Mechanical	FL0098	Seat not adjusting @ battery bay	0.87
Mechanical	FL0108	Red stop light @ R5 67S 41W	11.72
Strata	FL0113	Strata system faulty @ MW road	3.73

UTILITY SECTION PERFORMANCE OVERVIEW

✓
57
Available

Overall Fleet Availability

86%

57 of 66 units available



9

Unavailable

Area / Owner	Mon	Tue	Wed	Thu	Fri	Weekly Av. Avail.
Main West	1/2	1/2	1/2	1/2	2/2	70.0%
Boilermaker	2/3	2/3	2/3	2/3	2/3	66.7%
BEV	2/2	2/2	1/2	1/2	2/2	80.0%
Security	1/1	1/1	1/1	1/1	1/1	100.0%
Logistics	6/7	6/7	6/7	6/7	6/7	85.7%
Hyd Fitter	6/6	6/6	6/6	6/6	6/6	100.0%
Electricians	3/4	4/4	4/4	4/4	4/4	95.0%
Mechanics	3/3	3/3	3/3	3/3	3/3	100.0%
Sampling	2/2	2/2	2/2	2/2	2/2	100.0%
Construction	3/3	3/3	3/3	3/3	3/3	100.0%
Plant Fitter	6/7	6/7	6/7	6/7	6/7	85.7%
Central	1/2	1/2	1/2	1/2	2/2	70.0%
Explosive	1/1	1/1	1/1	1/1	1/1	100.0%
X Cut	1/1	1/1	1/1	1/1	1/1	100.0%
Utility TMM	2/2	2/2	2/2	2/2	2/2	100.0%
Other	18/18	18/18	18/18	18/18	18/18	100.0%
TOTAL	60/66	62/66	58/66	58/66	56/66	89.1%

UTILITY SECTION: UNAVAILABILITY DETAILS

Week 35 - All Unavailable Units

⚠ Weekly Breakdown Summary

Area/Owner	TMM No.	Model	Description - EOS / Breakdown	Remarks / Comment
Main West	LD0520, LD0611	Maverick	Weekly Avg 70%	LD0520: Front axle (Mon-Tue), LD0611: Lights/Strata (Mon-Tue)
Boilermaker	LD0405	Maverick	Weekly Avg 66.7%	Engine commission (No communication between engine and machine)
BEV	LD0375, LD0645	Maverick	Weekly Avg 80%	LD0375: Clutch/Rear shock (Mon-Fri), LD0645: Strata (Mon)
Central	LD0572, LD0625	Maverick	Weekly Avg 70%	LD0572: Not starting/brake/ball joint (Mon), LD0625: Strata (Tue)

Note: 1 unit(s) require OEM assistance

UTILITY SECTION CURRENT STATUS

Friday, 27 February 2026

⚠️ Unavailable Units by Area/Owner

Area/Owner	Unavailable	Details (Unit - Reason/Comment)
BEV	1	LD0375 - Clutch / Rear shock - (SOS - EOS)
Boilermaker	1	LD0405 - Engine commission (No communication between engine and machine) - No solution from Fernel (Deutz EMR4 upgrade to EMR5)
Construction	2	LD0574 - Not Starting - (SOS - EOS) - New wiring of Gas Level is draining battery LD0606 - Hub broken off - (SOS - EOS) - Waiting for parts
Seam 2	1	LD0622 - Transfer box leaking oil - (SOS - EOS) - Waiting for Transfer box
Sampling	1	UV0075 - Not Starting/Can bus faulty - (SOS - EOS)
Plant Fitter	1	UV0088 - Warning signs - (SOS - EOS)
Survey	1	UV0101 - Basket & outriggers malfunctioning - (SOS - EOS)
Logistics	1	UV0116 - Front axle - (SOS - EOS) - Waiting for front axle

Total Unavailable: 9 units across 8 areas
